

PROJECTS - TOMMY B 21

WESTERN B 22

I MAPPING

1:1000 scale mapping has been completed over much of Tommy and the east side of the Western claims.

The quartz vein system on Tommy has been defined over a strike length of 700 meters. Measured sections show widths of about 120 meters. Vein densities expressed a percent of quartz vein material over measured sections vary from 0.6% and 0.8% at the north and south ends to a high of 2.0% over 25 meters at adit creek.

Five road accessible drill sites have been laid out to test the Tommy zone over a strike length of 500 meters.

Mapping on Western shows fault offset vein packages of the same type as those of Tommy but generally narrower and of lesser vein density. The upper Guppy showing is 16.6 meters wide with a vein density of 3.4%. Comparative figures at measured sections north of this are:

Road cut at 6800N	13.4 meters	1.1%
Grid line 60N	17.2 meters	0.3%
" "	16.0 meters	0.3%
LAT 8200N	27.7 meters	0.4%

The vein package exposed along the highway within the Rose Marie crown grant measured 144 meters at 1.12% quartz vein.

Prospecting south of the upper Guppy showing has not revealed any extension of the vein system.

Hand sampling of the vein systems is in progress. Composite samples are cut which comprise material from each recognizable "T Type" (Tommy Type) vein within three meter wide sections. Additional samples from each 3 meter width comprise chips across the meter vein lithology.

II DRILLING : (fig 1)

- ACCESS :

A contract for equipment and operators at hourly rates was signed with Gibson Brothers Contractors Ltd of Tofino on June 23.

Work to be done includes :

- cleanup of existing spur roads
- add top gravel to washed out sections
- bridge Walkout Creek
- new spur roads to drill sites C, D, E.
- level out drill sites A to E
- access to river for water supply pump.

Estimated time for this program 4 to 5 days.
Estimated cost \$5000.00

On-site work began on June 24

- AGENCIES & INDIVIDUALS ADVISED OF IMMINENT DRILLING

- M&B - Kennedy Lake Division - Gary Patrucco 726-7712
Provided with map of access roads
- Fisheries and Oceans - Douglas Swift, Tofino 725-3468
Tour of proposed access and drill sites on June 23
Care must be taken to assure that no fuel, drilling mud, or silt gets into the Kennedy River.
- BC Forest Service - Alberni Ray Sorensen 7249205
We can expect inspections at any time during program re fire suppression requirements.

- Advance Drilling, Jack McCutcheon 888-0033
 Advised that we will be ready to drill
 any time after July 1. Expected arrival
 of equipment at Tommy July 3

III CLAIMS AND SUBMITTALS

- Wm:

A letter of intent re the option of
 Wm and Wm 2 claims of Walter Guppy
 was signed by Guppy on June 18, 1987.

- Au CLAIMS, Multinational Resources Inc

An east-west shear zone within
 granodiorite hosts gold bearing quartz veins
 over an explored length of 550 meters.

The shear zone is approximately 10 meters
 wide. Alteration shows a progressive zonation
 from chloritization to brecciation to
 intense silicification and sericitization
 enveloping a core of quartz vein.

~~The vein widths average 0.3 meters, maximum
 about 1.0 meter.~~

Vein widths on surface average 0.5 meters
 and 0.6 opt Au. Intersections from
 6 shallow drill holes averaged 0.7 meters
 at 0.25 opt Au.

An examination of the property on
 June 24 was specifically aimed at locating
 cross structures and quartz veins similar
 to those of the Tommy zone. Although
 it was found that the shear zone and
 host granodiorite is exposed almost continuously
 along the ~~the~~ 500 meter length of the
 drill explored extension no evidence of
 cross veining was seen.

Potential here appears to be similar to
 the Bear, Rose Marie etc ie that of narrow
 high grade fissure zones.

Au Claims Cont.

Ref: P. Folk P Eng April 1984
Report on the Geological, Geochemical
Magnetometer surveys, and Diamond Drilling
conducted on the Au 1-B Claim.

IV PERSONNEL

Patrick Harness left our employ in
to go commercial fishing. No replacement
is needed at present.



D. H. H.
Uclulet BC
June 25 / 87

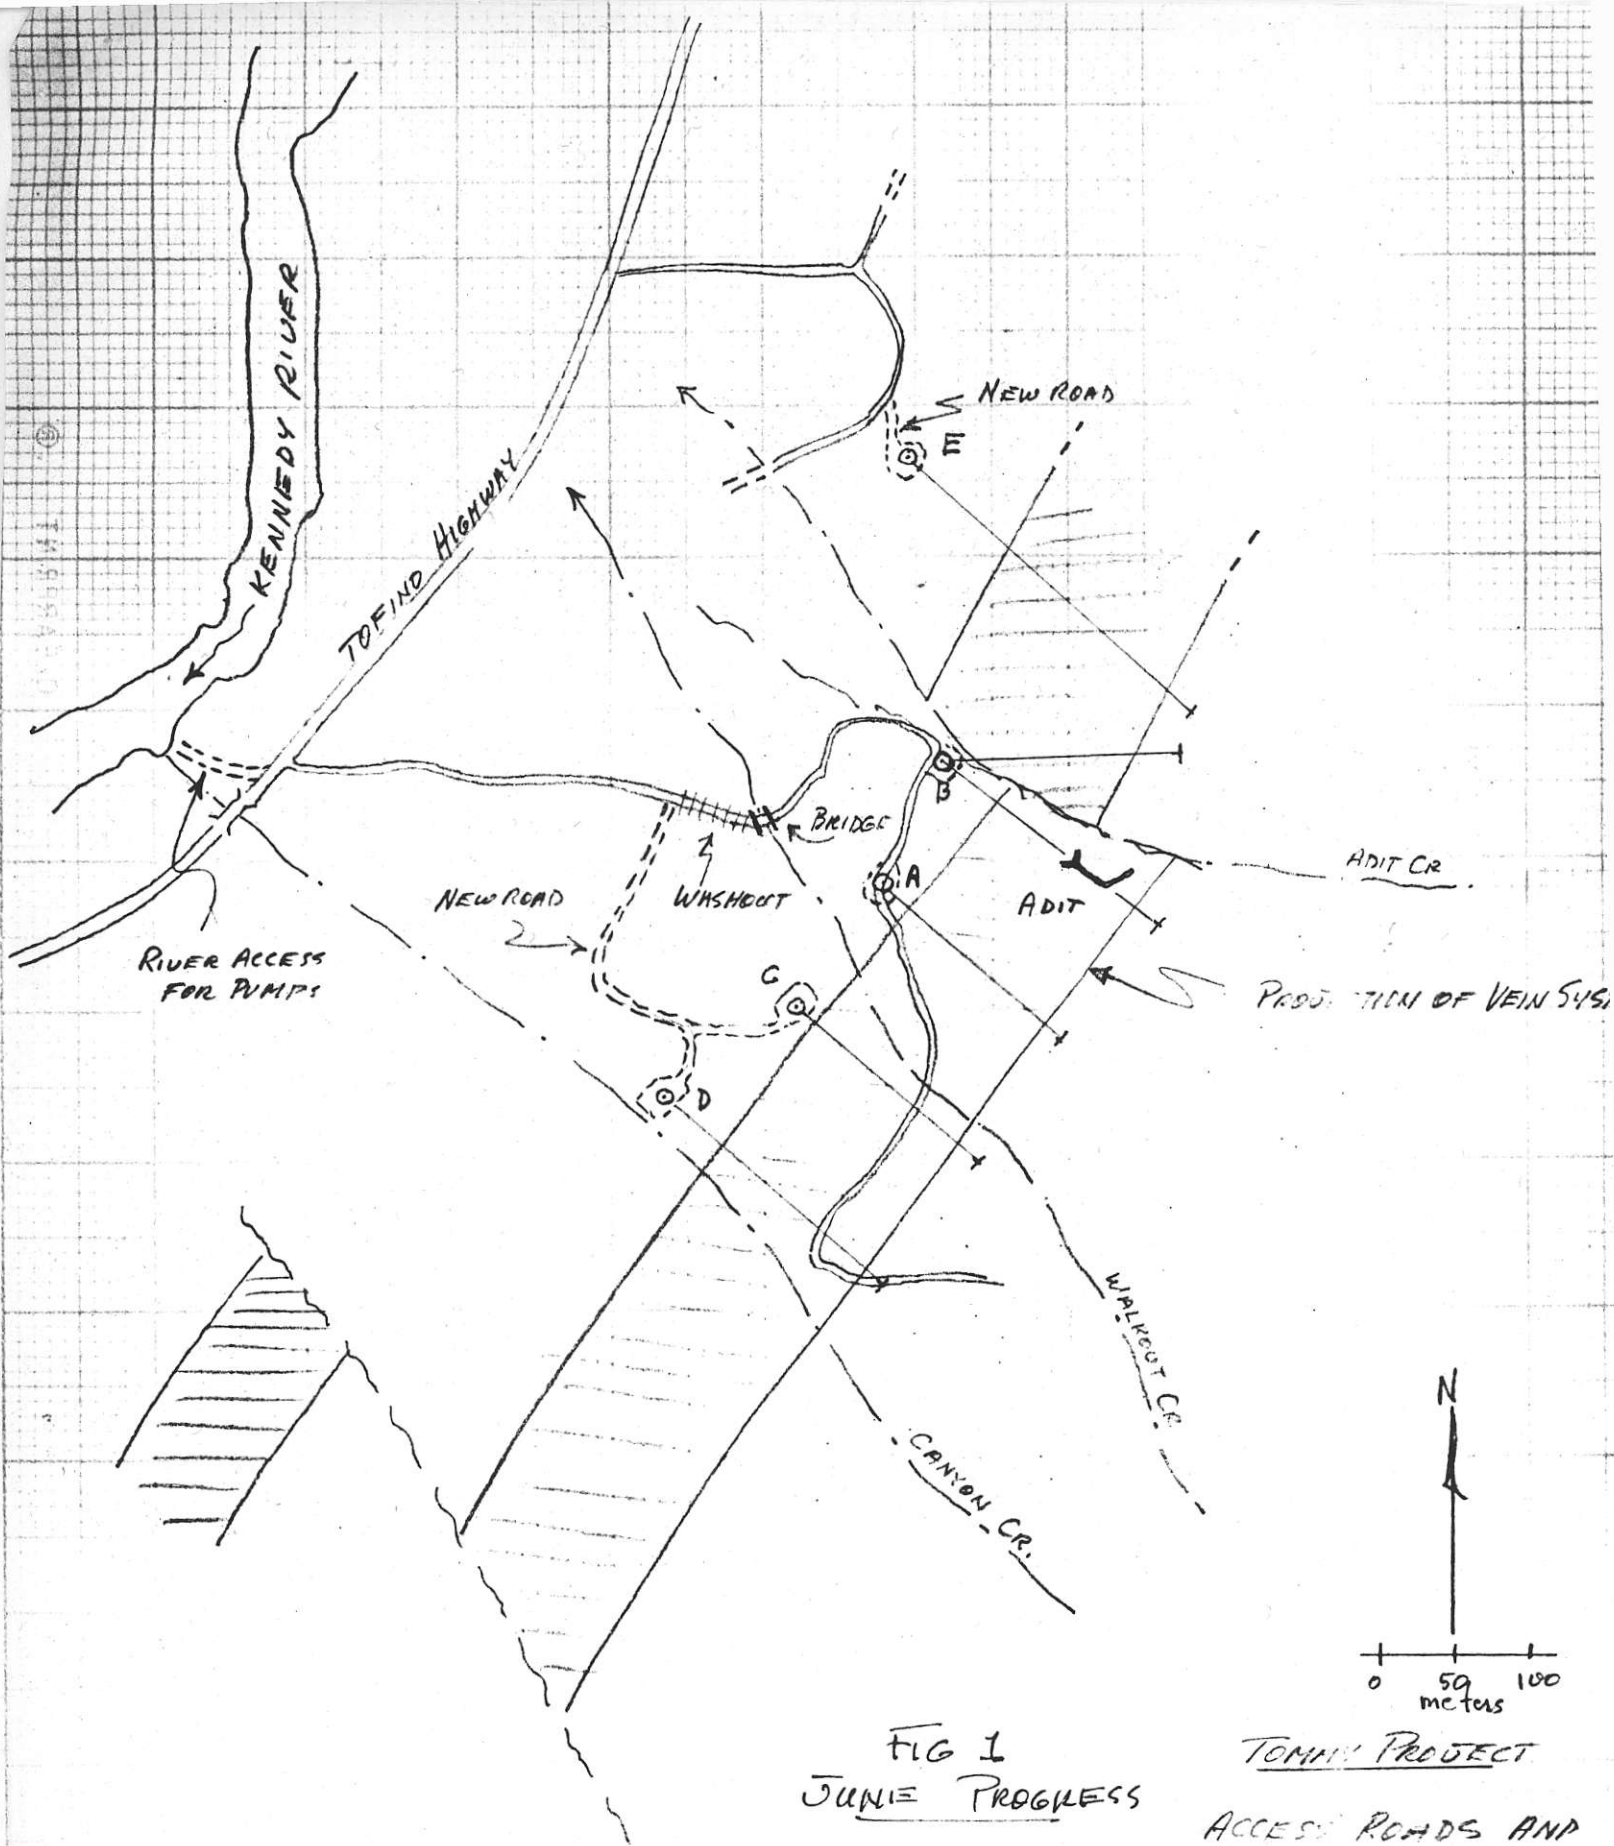


FIG 1
JUNE PROGRESS

TOMMY PROJECT

ACCESS ROADS AND
 DRILL SITES

SCALE 1:5000

RP June 24/87
