


# MAP - SHOWING TRENCHED AREAS

MAP NA  
103P 031

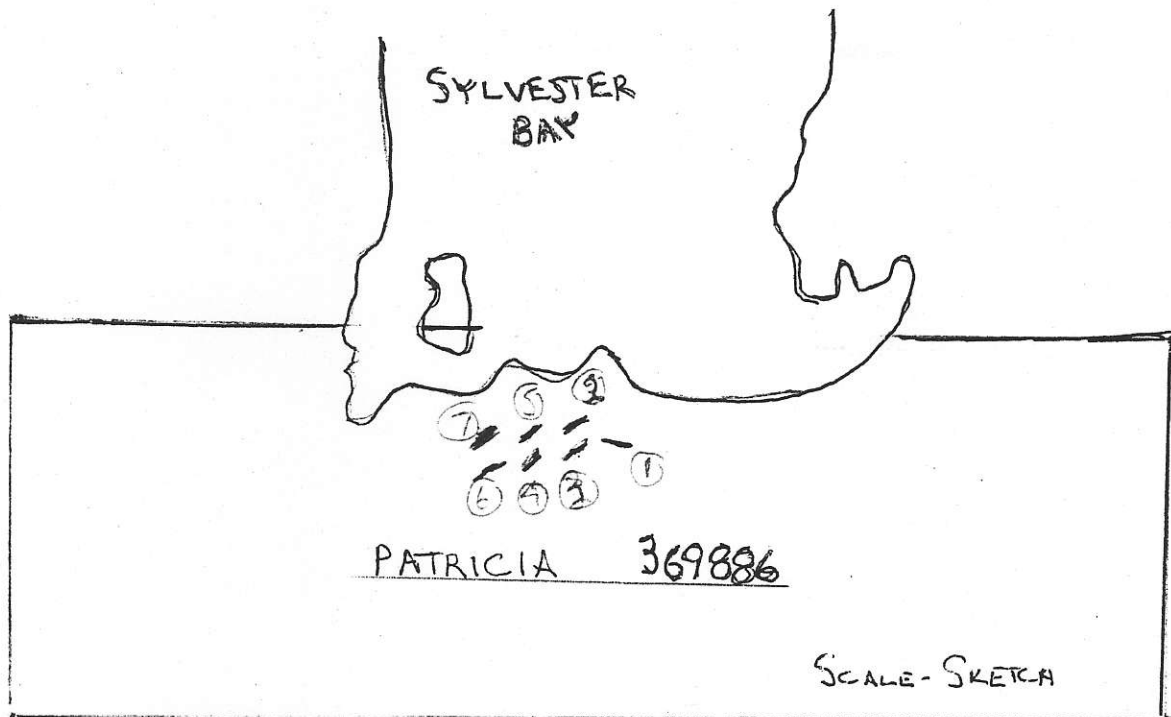

TRENCH #	LENGTH	WIDTH	DEPTH	TOTAL CU METRES	VALUE @ \$65 C.U.M.
1	8 m	3 m	2 m	48	3,120
2	12 m	2 m	2 m	48	3,120
3	10 m	2 m	2 m	40	2,600
4	7 m	3 m	2 m	42	2,730
5	8 m	3 m	2 m	48	3,120
6	12 m	2 m	1.5 m	36	2,340
7	8 m	3 m	1.5 m	36	2,340

TOTAL VALUE @ \$65 CUMETRE \$19,370

2 MEN WORKING USING PICKS & SHOVELS. BLAST HOLES ESTABLISH BY USING ALUMINUM + WOODEN TAMPERS. 40% FORTITE EXPLOSIVES USING "B" LINE & #6 CAPS TO DETONATE WORK CARRIED OUT BETWEEN JUL 14 - AUG 1, 2003.

VALUE OF \$65 CU METRE BLASTED ROCK USED TO ESTABLISH COST. ALL TRENCHES MARKED WITH RED & BLUE FLAGGING.
